FOOD ORDER MANAGEMENT SYSTEM Dashboard

Project Summary

Start Date: 02-09-2022

Finish Date: 31-10-2022

Duration: 2 Months

Completion Status: 85%
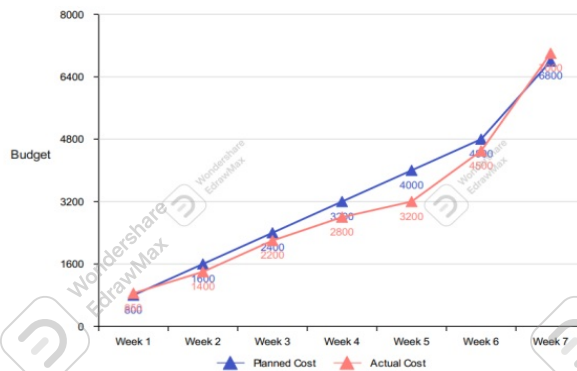
Budget: 8000

Project Completion Status

85%

● Average Online Orders

● Average number of Hotels

Kondhwa	55 / 30
Hadapsar	75 / 40
Kothrud	65 / 40

(bar chart axis: 0, 20, 40, 60, 78)

Line chart

(Line chart — Budget axis: 0, 1600, 3200, 4800, 6400, 8000; Weeks 1–7)

Planned Cost values: 800, 1600, 2400, 3200, 4000, 4800, 6800
Actual Cost values: 800, 1400, 2200, 2800, 3200, 4600, 6800

▲ Planned Cost   ▲ Actual Cost

Earn value analysis

$EV = 6800$

$PV = 6800$

$CV = -200$

$SV = 0$

$CPI = 0.971$

$SPI = 1$

$EAC = 8238.92$

(Pie chart values: 180, 120, 90, 75, 50)

● Planning   ● Resource Allocation   ● Testing

● Execution   ● Project Monitor
